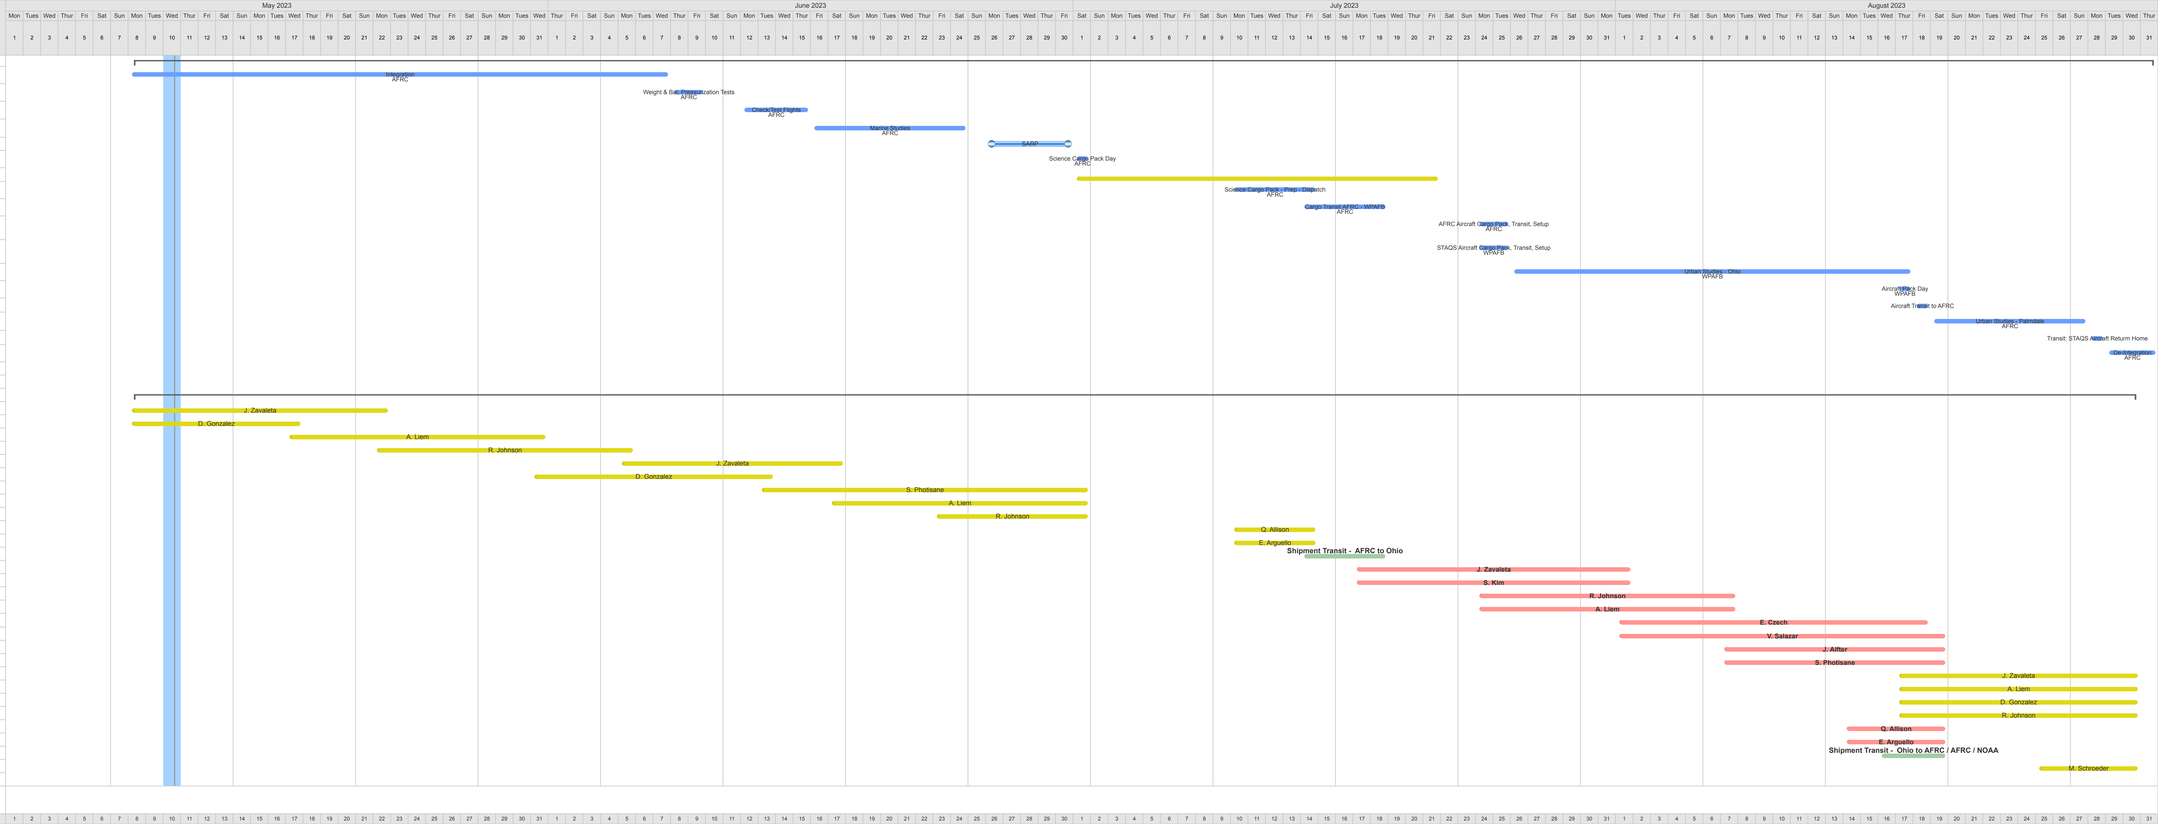	Activity Name	Duration (Days)	Start Date	Finish Date	Location	Resources Assigned
1	AEROMMA OVERALL SCHEDULE	**116.00**	**5/8/23**	**8/31/23**		
2	Integration	31.00	5/8/23	6/7/23	AFRC	
3	Weight & Bal, Pressurization Tests	2.00	6/8/23	6/9/23	AFRC	
4	Check/Test Flights	4.00	6/12/23	6/15/23	AFRC	
5	Marine Studies	9.00	6/16/23	6/24/23	AFRC	
6	SARP	5.00	6/26/23	6/30/23	AFRC	
7	Science Cargo Pack Day	1.00	7/1/23	7/1/23	AFRC	
8	Ops Hiatus	21.00	7/1/23	7/21/23	AFRC	
9	Science Cargo Pack - Prep - Dispatch	5.00	7/10/23	7/14/23	AFRC	
10	Cargo Transit AFRC - WPAFB	5.00	7/14/23	7/18/23	AFRC	
11	AFRC Aircraft Cargo Pack, Transit, Setup	2.00	7/24/23	7/25/23	AFRC	
12	STAQS Aircraft Cargo Pack, Transit, Setup	2.00	7/24/23	7/25/23	WPAFB	
13	Urban Studies - Ohio	23.00	7/26/23	8/17/23	WPAFB	
14	Aircraft Pack Day	1.00	8/17/23	8/17/23	WPAFB	
15	Aircraft Transit to AFRC	1.00	8/18/23	8/18/23		
16	Urban Studies - Palmdale	9.00	8/19/23	8/27/23	AFRC	
17	Transit: STAQS Aircraft Return Home	1.00	8/28/23	8/28/23		
18	De-Integration	3.00	8/29/23	8/31/23	AFRC	
19						
55						
56	ESPO STAFFING	**115.00**	**5/8/23**	**8/30/23**		
57	Integration & Test Flights	15.00	5/8/23	5/22/23	AFRC	J. Zavaleta
58	Integration & Test Flights	10.00	5/8/23	5/17/23	AFRC	D. Gonzalez
59	Integration - Test Flights & Marine	15.00	5/17/23	5/31/23	AFRC	A. Liem
60	Integration - Test Flights & Marine	15.00	5/22/23	6/5/23	AFRC	R. Johnson
61	Marine Studies	13.00	6/5/23	6/17/23	AFRC	J. Zavaleta
62	Marine Studies	14.00	5/31/23	6/13/23	AFRC	D. Gonzalez
63	Marine Studies	19.00	6/13/23	7/1/23	AFRC	S. Photisane
64	Urban Studies	15.00	6/17/23	7/1/23	AFRC	A. Liem
65	Urban Studies	9.00	6/23/23	7/1/23	AFRC	R. Johnson
66	Shipment Prep - AFRC to Ohio	5.00	7/10/23	7/14/23	AFRC	Q. Allison
67	Shipment Prep - AFRC to Ohio	5.00	7/10/23	7/14/23	AFRC	E. Arguello
68	Shipment Transit - AFRC to Ohio	5.00	7/14/23	7/18/23	AFRC	
69	Site Setup & Deployment Urban Studies	16.00	7/17/23	8/1/23	Ohio	J. Zavaleta
70	Site Setup & Deployment Urban Studies	16.00	7/17/23	8/1/23	Ohio	S. Kim
71	Deployment Urban Studies - Ohio	15.00	7/24/23	8/7/23	Ohio	R. Johnson
72	Deployment Urban Studies - Ohio	15.00	7/24/23	8/7/23	Ohio	A. Liem
73	Deployment Urban Studies - Ohio	18.00	8/1/23	8/18/23	Ohio	E. Czech
74	Deployment Urban Studies - Ohio	19.00	8/1/23	8/19/23	Ohio	V. Salazar
75	Deployment Urban Studies - Ohio	13.00	8/7/23	8/19/23	Ohio	J. Alfter
76	Deployment Urban Studies - Ohio	13.00	8/7/23	8/19/23	Ohio	S. Photisane
77	Deployment Urban Studies - AFRC	14.00	8/17/23	8/30/23	AFRC	J. Zavaleta
78	Deployment Urban Studies - AFRC	14.00	8/17/23	8/30/23	AFRC	A. Liem
79	Deployment Urban Studies - AFRC	14.00	8/17/23	8/30/23	AFRC	D. Gonzalez
80	Deployment Urban Studies - AFRC	14.00	8/17/23	8/30/23	AFRC	R. Johnson
81	Urban Studies - Shipment	6.00	8/14/23	8/19/23	Ohio	Q. Allison
82	Urban Studies - Shipment	6.00	8/14/23	8/19/23	Ohio	E. Arguello
83	Shipment Transit - Ohio to AFRC /	4.00	8/16/23	8/19/23	AFRC	
84	De-Integration, Shipment Arrival &	6.00	8/25/23	8/30/23	AFRC	M. Schroeder
85
